

McGee & Associates

Landscape Architecture

Project: GOLDEN GATE BEAUTIFICATION, M.S.T.U.
Project Manager: Darryl Richards, r.l.a., C.C.P.S.D. – A.T.M. Dept.
Consultant: McGee & Associates
Contractor: Hannula Landscaping & Irrigation Inc.
Report Period: May 2013

Location: Sunshine Blvd.
Consultant's Representative: Michael A. McGee, rla, isa
Contractor's Representative: Jeremy and Dale Hannula

Report No.: Eight
C - Indicates items to be addressed by Contractor

S - Indicates items to be addressed by staff.

Contractor is requested to address items as soon as possible and indicate in **RESPONSE/COMMENTS** column when items are addressed. Please return electronic copy to our office prior to next month's MSTU site review and meeting. **Note:** Copy picture out of comment boxes and then paste to additional sheet if picture is desired in larger size.

<u>LOCATION/WORK AREA</u>	<u>S</u>	<u>C</u>	<u>R</u>	<u>MAINTENANCE SERVICES OBSERVATIONS & RECOMMENDATIONS</u>	<u>RESPONSE or COMMENTS</u>
Observation date: 05/13-14/13				<u>MONTHLY ADDRESSED</u>	Please provide responses as will review, ongoing, completed or proposal to be submitted. Once submitted provide proposal number and date and any notation deemed important.
Median #1		X		Continue treatments on Indian Hawthorn shrubs.	
Median #2		X		Turf has multiple areas of water stressed grass. Please review coverage and make recommendations for replacement head types and/or additional heads to provide full coverage.	Schedule meeting with Maintenance Consultant to review in field.
		X		Hand remove weeds in Indian hawthorn.	
		X	2	Continue treatments on Indian Hawthorn shrubs. Remove volunteer Tomato plant in Indian Hawthorn on north end.	
Median #3		X		Turf has multiple areas of water stressed grass. Please review coverage and make recommendations for replacement head types and/or additional heads to provide full coverage.	Schedule meeting with Maintenance Consultant to review in field.
		X		Continue treatments on Indian Hawthorn shrubs.	
	X		5	On the south end of median light pole B2 has the access door cover missing and wires are exposed. (photo)	
Median #4		X		Remove dead Indian hawthorn and replant with 3 gal. size.	
		X		Continue treatments on Indian Hawthorn shrubs.	
Median #5		X		Hand remove weeds in Indian hawthorn.	
		X		Continue treatments on Indian Hawthorn shrubs. Prune dead foliage off plants.	
		X	2	Remove Oak tree seedlings or sprouts.	
Median #6		X		Turf has multiple areas of water stressed grass. Please review coverage and make recommendations for replacement head types and/or additional heads to provide full coverage.	Schedule meeting with Maintenance Consultant to review in field.
		X		Hand remove weeds and prune out dead foliage in Juniper south end.	
		X		Continue treatments on Indian Hawthorn shrubs.	



Design * Environmental Management * Planning * Arborist

5079 Tamiami Trail East / P. O. Box 8052 Naples, Florida 34101
 Phone (239) 417-0707 * Fax (239) 417-0708
 LC 098 * FL 1023A

McGee & Associates

Landscape Architecture

GOLDEN GATE BEAUTIFICATION, M.S.T.U.

Location: Sunshine Blvd.

Report Period: May 2013

Report No.: Eight

<u>LOCATION/WORK AREA</u>	<u>S</u>	<u>C</u>	<u>R</u>	<u>MAINTENANCE SERVICES OBSERVATIONS & RECOMMENDATIONS</u>	<u>RESPONSE or COMMENTS</u>
18 th Place SW Median					
				<u>QUARTERLY ADDRESSED</u>	
Median #1, 2, 3 & 6					
Pump Station-Median #3, 5 hp , 6" well, VFD					
Lighting Electric Meter 2271 Sunshine Blvd., 1 SUN, Alley off 23 rd Ave. SW					
Lighting Electric Meter & Irrigation Controller Electric , 1995 Sunshine Blvd., 2 SUN, Alley off 20 th PL. SW					
Lighting Electric Meter 4642 18 th Pl. SW, 3 SUN, North R/W					
Fertilizations:		X		Schedule for May: Turf – 15-0-15, 6.5 lbs. per 1000 S.F. (5-50 lbs. bags). Shrubs & Ground Covers: 8-2-12-180, 15 lbs. per 1000 S.F. (7-50 lb. bags) Please place request for materials from staff.	
Irrigation:		X		Turf has multiple areas of water stressed grass. Please review coverage and make recommendations for replacement head types and/or additional heads to provide full coverage.	Schedule meeting with Maintenance Consultant to review in field.

McGee & Associates

Landscape Architecture

GOLDEN GATE BEAUTIFICATION, M.S.T.U.


Location: Sunshine Blvd.

Report Period: May 2013

Report No.: Eight

LOCATION/WORK AREA	S	C	R	MAINTENANCE SERVICES OBSERVATIONS & RECOMMENDATIONS	RESPONSE or COMMENTS
--------------------	---	---	---	---	----------------------

GG MSTU Sunshine Blvd. Well Annual Water Use for 2013

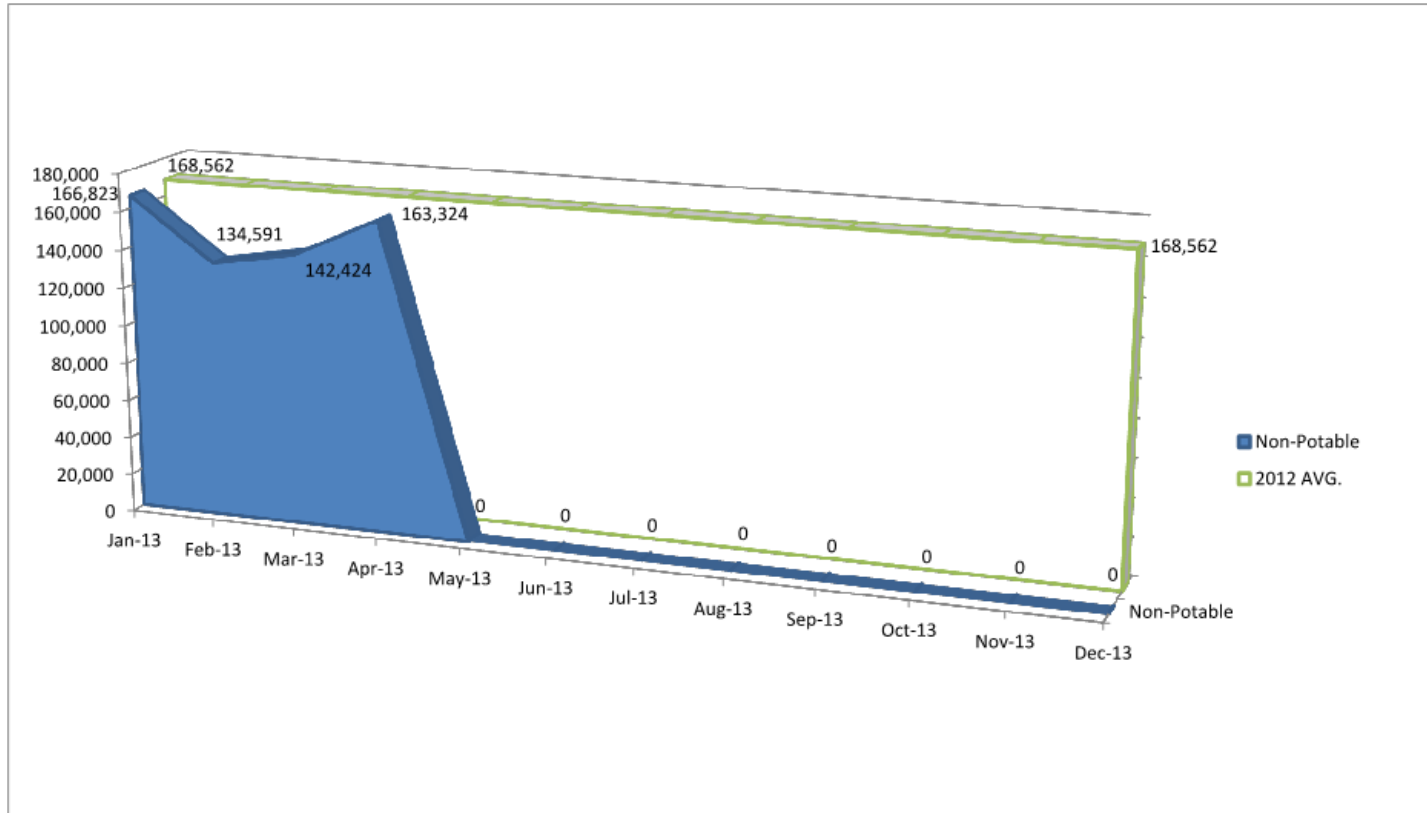

Water Use Goal:

(1.47 ac. of Plants & Turf)

Recommended: Supplemental watering rate of .75 to 1 inch per week. One inch per week equals 39,917 gallons per week or 159,668 gallons per month.

2012 total water use: 2,022,743 gallons or 50.67 inches of supplemental water pumped.

5/01/2013
