

McGee & Associates

Landscape Architecture

Project: GOLDEN GATE BEAUTIFICATION, M.S.T.U.
Project Manager: Darryl Richards, r.l.a., C.C.P.S.D. – A.T.M. Dept.
Consultant: McGee & Associates
Contractor: Hannula Landscaping & Irrigation Inc.
Report Period: June 2013

Location: Sunshine Blvd.
Consultant's Representative: Michael A. McGee, rla, isa
Contractor's Representative: Jeremy and Dale Hannula

Report No.: Nine
C - Indicates items to be addressed by Contractor

S - Indicates items to be addressed by staff.

Contractor is requested to address items as soon as possible and indicate in **RESPONSE/COMMENTS** column when items are addressed. Please return electronic copy to our office prior to next month's MSTU site review and meeting. **Note:** Copy picture out of comment boxes and then paste to additional sheet if picture is desired in larger size.

<u>LOCATION/WORK AREA</u>	<u>S</u>	<u>C</u>	<u>R</u>	<u>MAINTENANCE SERVICES OBSERVATIONS & RECOMMENDATIONS</u>	<u>RESPONSE or COMMENTS</u>
Observation date: 06/13-17/13				<u>MONTHLY ADDRESSED</u>	Please provide responses as will review, ongoing, completed or proposal to be submitted. Once submitted provide proposal number and date and any notation deemed important.
Median #1		X		Continue treatments on Indian Hawthorn shrubs.	Treatments are continuously being performed on a monthly basis
Median #2		X		Turf has multiple areas of water stressed grass. Please review coverage and make recommendations for replacement head types and/or additional heads to provide full coverage.	7/11/13: Median# 2 - there's head to head coverage and there's no need replace head types or add additional coverage. We'd cleaned around the heads and will be replacing any heads that are too low in the ground during weekly service. Irrigation watering increase was requested during stress. I did noticed grub in the turf, please advise pest control to review.
		X	2	Hand remove weeds in Indian hawthorn.	Completed
Median #3	X		6	On the south end of median light pole B2 has the access door cover missing and wires are exposed.(photo)	7/11/13: Median #6 heads were cleaned and will replace any head that's too low in the ground during weekly service . Irrigation watering increase was requested during stress.
Median #4		X	2	Remove dead Indian hawthorn and replant with 3 gal. size.	Completed
Median #5					
Median #6		X	2	Turf has multiple areas of water stressed grass. Please review coverage.	
18 th Place SW Median					
				<u>QUARTERLY ADDRESSED</u>	
Pump Station-Median #3, 5 hp , 6" well, VFD					
Lighting Electric Meter 2271 Sunshine Blvd., 1 SUN, Alley off 23rd					



Design * Environmental Management * Planning * Arborist

5079 Tamiami Trail East / P. O. Box 8052 Naples, Florida 34101
 Phone (239) 417-0707 * Fax (239) 417-0708
 LC 098 * FL 1023A

McGee & Associates

Landscape Architecture

GOLDEN GATE BEAUTIFICATION, M.S.T.U.

Location: Sunshine Blvd.

Report Period: June 2013

Report No.: Nine

<u>LOCATION/WORK AREA</u>	<u>S</u>	<u>C</u>	<u>R</u>	<u>MAINTENANCE SERVICES OBSERVATIONS & RECOMMENDATIONS</u>	<u>RESPONSE or COMMENTS</u>
Ave. SW					
Lighting Electric Meter & Irrigation Controller Electric , 1995 Sunshine Blvd., 2 SUN, Alley off 20 th PL. SW					
Lighting Electric Meter 4642 18 th Pl. SW, 3 SUN, North R/W					
Fertilizations:		X		Schedule for May: Turf – 15-0-15, 6.5 lbs. per 1000 S.F. (5-50 lbs. bags). Shrubs & Ground Covers: 8-2-12-180, 15 lbs. per 1000 S.F. (7-50 lb. bags) Please place request for materials from staff.	completed
Irrigation:					

McGee & Associates

Landscape Architecture

GOLDEN GATE BEAUTIFICATION, M.S.T.U.


Location: Sunshine Blvd.

Report Period: June 2013

Report No.: Nine

LOCATION/WORK AREA	S	C	R	MAINTENANCE SERVICES OBSERVATIONS & RECOMMENDATIONS	RESPONSE or COMMENTS
--------------------	---	---	---	---	----------------------

GG MSTU Sunshine Blvd. Well Annual Water Use for 2013

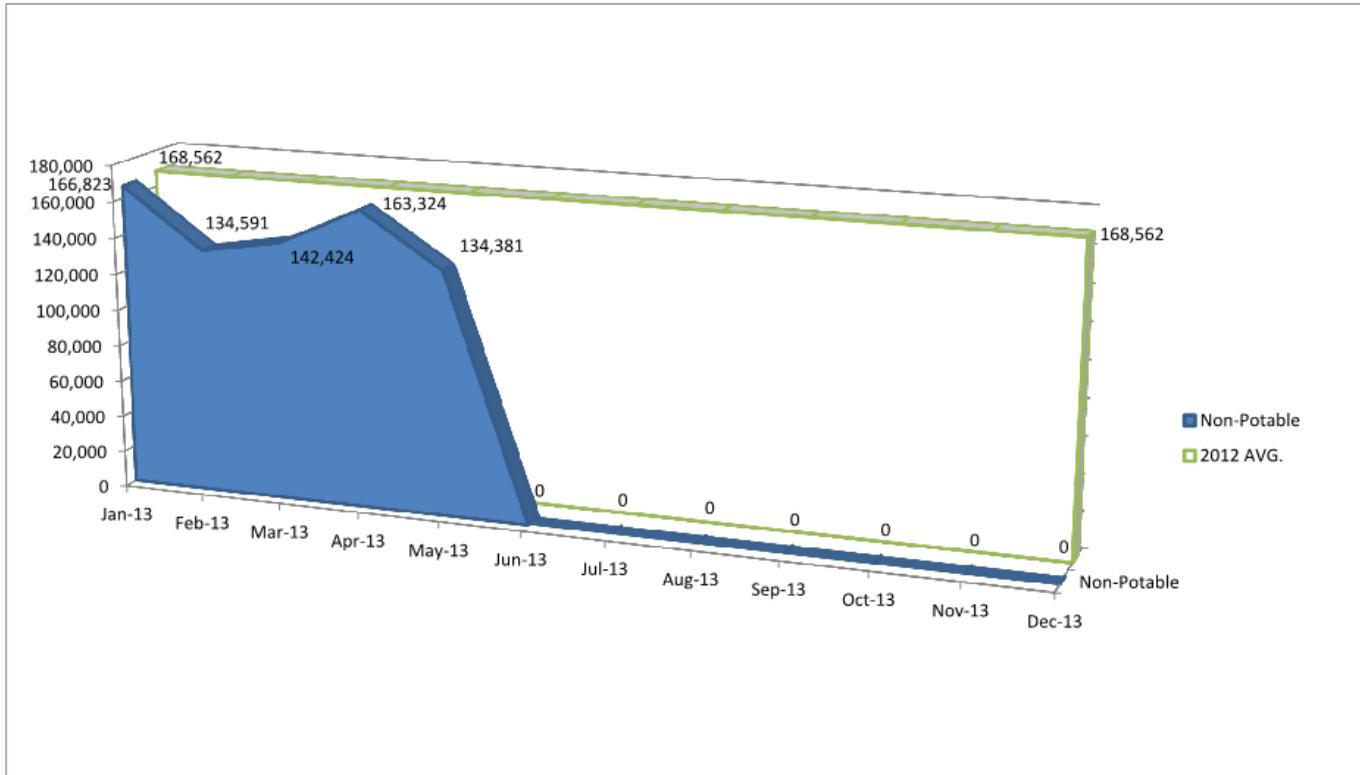

Water Use Goal:

(1.47 ac. of Plants & Turf)

Recommended: Supplemental watering rate of .75 to 1 inch per week. One inch per week equals 39,917 gallons per week or 159,668 gallons per month.

2012 total water use: 2,022,743 gallons or 50.67 inches of supplemental water pumped.

6/03/2013
