

McGee & Associates

Landscape Architecture

Project: GOLDEN GATE BEAUTIFICATION, M.S.T.U.
Project Manager: Darryl Richards, r.l.a., C.C.P.S.D. – A.T.M. Dept.
Consultant: McGee & Associates
Contractor: Hannula Landscaping & Irrigation Inc.
Report Period: FY 13-14, October 2013

Location: Sunshine Blvd.
Consultant's Representative: Michael A. McGee, rla, isa
Contractor's Representative: Jeremy and Dale Hannula

Report No.: One - FY 13-14

S - Indicates items to be addressed by staff.

C - Indicates items to be addressed by Contractor

Contractor is requested to address items as soon as possible and indicate in **RESPONSE/COMMENTS** column when items are addressed. Please return electronic copy to our office prior to next month's MSTU site review and meeting. **Note:** Copy picture out of comment boxes and then paste to additional sheet if picture is desired in larger size.

<u>LOCATION/WORK AREA</u>	<u>S</u>	<u>C</u>	<u>R</u>	<u>MAINTENANCE SERVICES OBSERVATIONS & RECOMMENDATIONS</u>	<u>RESPONSE or COMMENTS</u>
Observation date: 10/08-10/13				<u>MONTHLY ADDRESSED</u>	Please provide responses as will review, ongoing, completed or proposal to be submitted. Once submitted provide proposal number and date and any notation deemed important.
Median #1		X		Remove staking from Crape myrtle tree.	
		X	2	Schedule broadleaf weed treatments for turf a soon as weather permits.	
Median #2		X		At 20 th Ct. SW: Replace two dead Indian hawthorn. 3 gal. size.	
		X		Remove spider webs on south end light pole.	
		X	2	Schedule broadleaf weed treatments for turf a soon as weather permits.	
Median #3		X	2	Schedule broadleaf weed treatments for turf a soon as weather permits.	
Median #4		X	2	Remove spider webs on south end light pole.	
		X	6	Remove dead Indian hawthorn and replant with 3 gal. size.	Hannula 9-5-13: Removal Completed; Replacements (7) Indian Hawthorns – Estimate #13-3250.
Median #5					
Median #6		X	2	Schedule broadleaf weed treatments for turf a soon as weather permits.	
		X		At address 1770: Replace dead Indian hawthorn. 3 gal. size.	
18 th Place SW Median					
				<u>QUARTERLY ADDRESSED</u>	
Accent/Street Lighting	X			Lights are on during the day: Median #1 north end; Median #2 south ends;	
Pump Station-Median #3, 5 hp , 6" well, VFD					
Lighting Electric Meter 2271 Sunshine Blvd., 1 SUN, Alley off 23rd Ave. SW					
Lighting Electric Meter & Irrigation Controller Electric , 1995 Sunshine Blvd., 2 SUN, Alley off 20th PL. SW					

Design * Environmental Management * Planning * Arborist

5079 Tamiami Trail East / P. O. Box 8052 Naples, Florida 34101

Phone (239) 417-0707 * Fax (239) 417-0708

LC 098 * FL 1023A

McGee & Associates

Landscape Architecture

GOLDEN GATE BEAUTIFICATION, M.S.T.U.


Location: Sunshine Blvd.

Report Period: FY 13-14, october 2013

Report No.: One

LOCATION/WORK AREA	S	C	R	MAINTENANCE SERVICES OBSERVATIONS & RECOMMENDATIONS	RESPONSE or COMMENTS
Lighting Electric Meter 4642 18 th Pl. SW, 3 SUN, North R/W					
Fertilizations:		X	2	Schedule for first week of October: Turf, Shrubs, Ground Covers & Blooming plants: Turf-15-0-15, 6.5 lbs. per 1,000 S.F. (5-50 lb. bags) Shrubs/Grn Covers – 8-2-12-180 'Florikote', 15 lbs. per 1,000 S.F. (7-50 lb. bags) Blooming plants - 14-14-14-90, 7 lbs. per 1,000 S.F. (1-50 lb. bags) Please place request for materials from staff.	M&A: 10-10-13 Please update status.
Irrigation:					

GG MSTU Sunshine Blvd. Well Annual Water Use for 2013

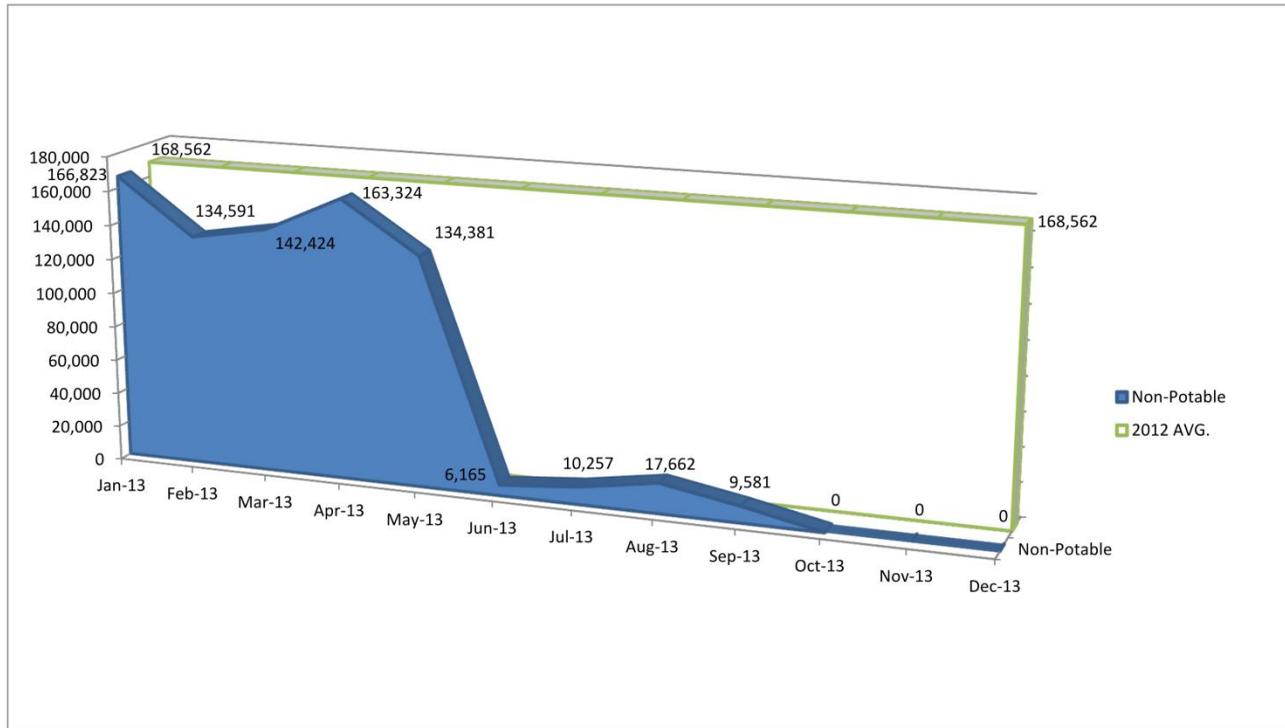

Water Use Goal:

(1.47 ac. of Plants & Turf)

Recommended: Supplemental watering rate of .75 to 1 inch per week. One inch per week equals 39,917 gallons per week or 159,668 gallons per month.

2012 total water use: 2,022,743 gallons or 50.67 inches of supplemental water pumped.

10/01/2013
