

Landscape Architecture

Project: GOLDEN GATE BEAUTIFICATION, M.S.T.U. Location: Tropicana Blvd.

Project Manager: Collier County Public Services Division, Public Transportation & Neighborhood Enhancements Department

Consultant: McGee & Associates Consultant's Representative: Michael A. McGee, rla, isa

Contractor:Green EffexContractor's Representative:John SauppReport Period:FY 18-19 May 2019Report No.:Eight

AC - Indicates major items recommended to be discussed by Advisory Committee, S - Indicates items recommended to be addressed by staff,

<u>C</u> - Indicates items recommended to be addressed by Contractor

MAINTENANCE ITEM	<u>AC</u>	<u>s</u>	<u>c</u>	<u>R</u>	SUMMARY OF MONTHLY	RESPONSE or COMMENTS
Observation date: 5/13/19					MAINTENANCE SERVICES OBSERVATIONS & RECOMMENDATIONS	Refer to monthly report for detailed information
TREES	Х	Х			See monthly detailed report for post hurricane Irma damage and recommendations.	See detailed report for Yellow - highlighted items that are renovation recommendations generally based upon hurricane Irma damage.
		Х	Х	10	At address 2836: One Holly tree has defoliated. Will review next report period.	M&A: 8/13/18 Tree is dead and needs to be removed and replaced.
						M&A: 3/11/19 Landscape renovation is in process.
SHRUBS, ORNAMENTAL GRASSES &		Х	Х	15	Dwarf Fakahatchee and some Bougainvillea beds need renovation. See monthly detailed report for post	M&A: 3/11/19 Landscape renovation is in process.
GROUND COVERS					hurricane Irma damage and recommendations.	
TURF		Х	Х		Broadleaf and dead weeds present in turf areas.	
IRRIGATION			Х		The previous month water use total per WeatherTrak data was 389,081 gallons.	
WEED CONTROL			Х		Volunteer plants, sprouts and weeds need to be addressed throughout several median beds.	
UNDERSTORY PRUNING			Х		No major issues observed	
DISEASE AND PEST CONTROL			Х		No major issues observed	
FERTILIZATION			Х		Review schedule for recommendations.	
ACCENT/STREET LIGHTING			Х		No major issues observed	



GOLDEN GATE BEAUTIFICATION, M.S.T.U.

Location: Tropicana Blvd.

Report Period: FY 18-19, May 2019


Report No.: Eight

SUMMARY OF MONTHLY

RESPONSE or COMMENTS

MAINTENANCE SERVICES OBSERVATIONS & RECOMMENDATIONS

GG MSTU TROPICANA Blvd. Well Annual Water Use for 2019

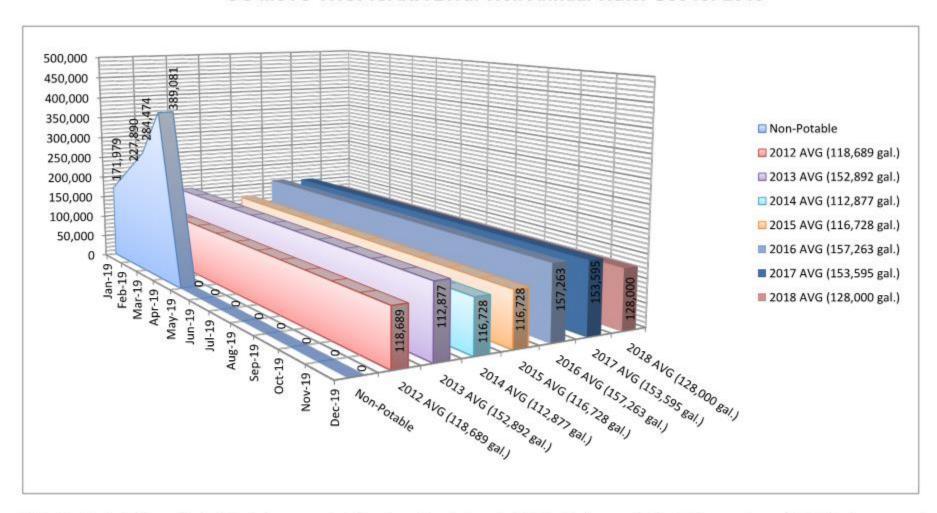

Water Use Goal: (1.35 ac. of Plants & Turf), Recommended: Supplemental watering rate of .75 to 1 inch per week. One inch per week equals 36,658 gallons per week or 146,633 gallons per month.

2012 total water use Jun. 2012 - Dec. 2012: 646,177 gallons or 17.63 inches of supplemental water pumped.

2013 total water use Jan. 2013 - Dec. 2013: 1,834,698 gallons or 50.04 inches of supplemental water pumped.

2014 total water use Jan. 2014 - Dec. 2014: 1,354,526 gallons or 36.95 inches of supplemental water pumped. 26% water use reduction

2015 total water use Jan. 2015 - Dec. 2015: 1,400,734 gallons or 38.21 inches of supplemental water pumped, 3% water use increase, Nov. & Dec. system not

functioning properly, 9/2016 new controller system activated, some readings based upon estimated projections.

2016 total water use Jan. 2016 - Dec. 2016: 1,887,160 gallons or 51.48 inches of supplemental water pumped.

2017 total water use Jan.2017-Dec. 2017: 1,843,140 gallons or 50.28 inches of supplemental water pumped.

2018 total water use Jan. 2018-Dec. 2018: 1,535,998 gallons or 41.90 inches of supplemental water pumped.

4/8/19
