

McGee & Associates

Landscape Architecture

Project: GOLDEN GATE BEAUTIFICATION, M.S.T.U.
Project Manager: Harry Sells, MSTU Project Manager, C.C.P.S.D. – P.T.N.E. Dept.
Consultant: McGee & Associates
Contractor: Hannula Landscaping & Irrigation Inc.
Report Period: FY 14-15, June 2015

Location: Sunshine Blvd.
Consultant's Representative: Michael A. McGee, rla, isa
Contractor's Representative: Dale Hannula
Report No.: Nine - FY14-15

S - Indicates items to be addressed by staff.

C - Indicates items to be addressed by Contractor

Contractor is requested to address items as soon as possible and indicate in **RESPONSE/COMMENTS** column when items are addressed. Please return electronic copy to our office prior to next month's MSTU site review and meeting. **Note:** Copy picture out of comment boxes and then paste to additional sheet if picture is desired in larger size.

LOCATION/WORK AREA	S	C	R	MAINTENANCE SERVICES OBSERVATIONS & RECOMMENDATIONS	RESPONSE or COMMENTS
Observation date: 06/08-11/15				MONTHLY ADDRESSED	Please provide responses as will review, ongoing, completed or proposal to be submitted. Once submitted provide proposal number and date and any notation deemed important.
Median 2, 3, & 6		X	3	It is recommended to apply to all dwarf Bougainvillea and any remaining Indian hawthorn beds Ferromec AC15-0-0 plus 6% iron & 3% sulfur @ 1.5 gal. per 100 gal. of water and root drench with Cleary's 3336 per manufacturer's recommended rate.	
Median #1		X	7	Two Juniper plants have been damaged and need to be replaced with 3 gal. size plants.	
Median #2		X		Yellow Alder tree has broken in half from heavy wind. (Photo)	It is recommended to remove and replace the tree location with a Tabebuia 'Ipe', 12'-14' oa. Ht.
		X	3	See above for Bougainvillea shrubs.	
		X	17	At address 2274: Replace auto accident damaged Juniper on south end of median.	M&A: Appears 3-3 gal. plants will be needed. M&A: 7/8/14 another accident has occurred in same location. Approx. 50 L.F. of Juniper damaged. Review and remove damaged and provide count for replacements. (photo)
Median #3		X	9	Light pole accident on south end of median. Multiple Juniper have been run over and are damaged and broken. Prune out damaged foliage and branches and review in 30 days for replacements.	M&A: 12-12-14 Damaged plants have been removed.
Median #4					
Median #5					
Median #6		X	3	See above for Bougainvillea and Indian hawthorn shrubs.	
18 th Place SW Median		X		Remove large weeds in pavers and Bougainvillea.	
		X	3	Remove damaged Bougainvillea branches and review for replacements. 3 gal. size.	
18th Ave. S.W. Median		X	14	Auto accident has removed 6 to 8 Bougainvillea plants on northwest side. Review and provide count for replacements.	M&A: 4/14/15 This location will now be listed in this report and not the Collier Blvd. Part B report.

Comment [MAM1]:



Comment [MAM2]:



Design * Environmental Management * Planning * Arborist

5079 Tamiami Trail East / P. O. Box 8052 Naples, Florida 34101
 Phone (239) 417-0707 * Fax (239) 417-0708
 LC 098 * FL 1023A

McGee & Associates

Landscape Architecture

GOLDEN GATE BEAUTIFICATION, M.S.T.U.

Location: Sunshine Blvd.

Report Period: FY 14-15, June 2015

Report No.: Nine

LOCATION/WORK AREA	S	C	R	MAINTENANCE SERVICES OBSERVATIONS & RECOMMENDATIONS	RESPONSE or COMMENTS
<u>QUARTERLY ADDRESSED</u>					
Accent/Street Lighting	X		7	In north end of median 3 light pole B-2 has been removed do to an accident. (photo)	M&A:06/11/15 Light pole debris is still in median.
Pump Station-Median #3, 5 hp , 6" well, VFD					
Lighting Electric Meter 2271 Sunshine Blvd., 1 SUN, Alley off 23rd Ave. SW					
Lighting Electric Meter & Irrigation Controller Electric , 1995 Sunshine Blvd., 2 SUN, Alley off 20th PL. SW					
Lighting Electric Meter 4642 18th Pl. SW, 3 SUN, North R/W					
Fertilizations:		X	2	Please update status of April's requirements and submit for May's requirements per schedule below.	
Irrigation:		X		Please perform a controller program review and complete check of the main line and zones to see if there are any leaks occurring during operations.	
	X	X	7	The water use for November was extremely high. Review system and controller for issues. If the Bermad pulse counter is working then request from Darryl's office to contact the County Irrigation Project Manager to set the maximum flow per week at 45,000 gallons at which time an alarm will be sent to Hannula Landscaping.	M&A: 4/15/15 Please update status.

Comment [MAM3]:



McGee & Associates

Landscape Architecture

GOLDEN GATE BEAUTIFICATION, M.S.T.U.


Location: Sunshine Blvd.

Report Period: FY 14-15, June 2015

Report No.: Nine

LOCATION/WORK AREA	S	C	R	MAINTENANCE SERVICES OBSERVATIONS & RECOMMENDATIONS	RESPONSE or COMMENTS
--------------------	---	---	---	---	----------------------

GG MSTU Sunshine Blvd. Well Annual Water Use for 2015

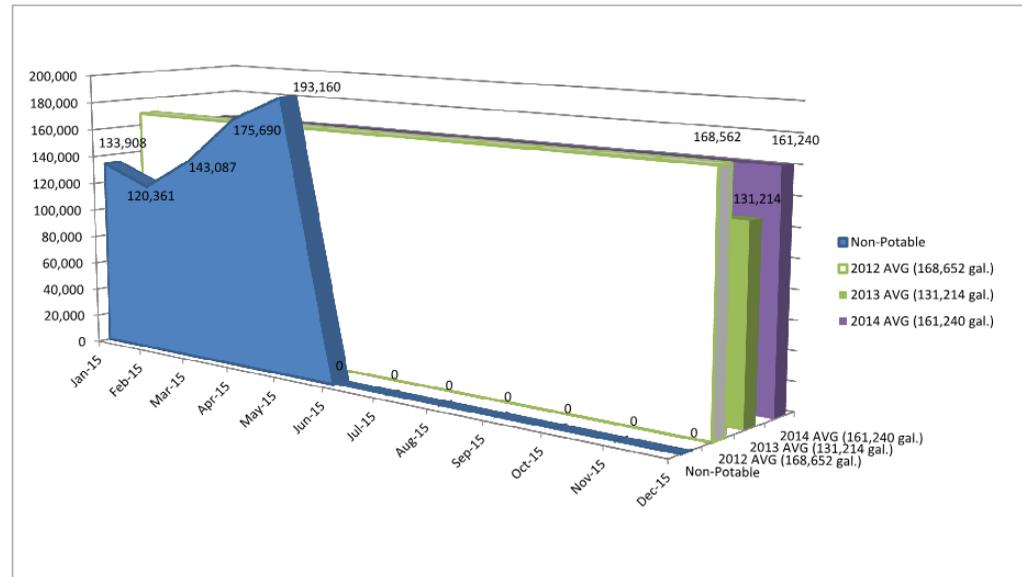

Water Use Goal:

(1.47 ac. of Plants & Turf)

Recommended: Supplemental watering rate of .75 to 1 inch per week. One inch per week equals 39,917 gallons per week or 159,668 gallons per month.

2012 total water use: 2,022,743 gallons or 50.67 inches of supplemental water pumped.

2013 total water use: 1,574,562 gallons or 39.45 inches of supplemental water pumped.

2014 total water use: 1,954,877 gallons or 48.97 inches of supplemental water pumped.

6/1/2015

GOLDEN GATE MSTU FY 14-15 RECOMMENDED FERTILIZATION SCHEDULE - SUNSHINE BLVD.				
Plant Type	Turf / St. Augustine	Palm Trees	Shrubs & Grn. Cover Beds	Blooming Plants
Areas	(39,520 S.F.)		(21,846 S.F.)	(5,500 S.F.)
Month				
Jan-15	15-0-15 for rotary spreader 6.5 lbs. per 1000 S.F. (5 - 50 lb. Bags)		8-2-12-180 (Florikote Collier blend) 15 lb. per 1000 S.F. (7 - 50 lb. bags)	14-14-14-90 7 lbs. per 1000 S.F. (1 - 50 lb. bag)
Feb-15				20-20-20 2.5 lbs./25 gal. H2O per 1000 S.F. (14 lbs.)
Mar-15	15-0-15 for rotary spreader 6.5 lbs. per 1000 S.F. (5 - 50 lb. Bags)			
Apr-15				14-14-14-90 7 lbs. per 1000 S.F. (1 - 50 lb. bag)
May-15	15-0-15 for rotary spreader 6.5 lbs. per 1000 S.F. (5 - 50 lb. Bags)		8-2-12-180 (Florikote Collier blend) 15 lb. per 1000 S.F. (7 - 50 lb. bags)	
Jun-15				
Jul-15				
Aug-15	0-0-22 SPM 1 lb. per 100 S.F. (8 - 50 lb. bags)		0-0-22 SPM 1 lb. per 100 S.F. (4 - 50 lb. bags)	0-0-22 SPM 1 lb. per 100 S.F. (1 - 50 lb. bags)
Sep-15	Place request for October 2015		Place request for October 2014	Place request for October 2014
10/1/2014-2015	15-0-15 for rotary spreader 6.5 lbs. per 1000 S.F. (5 - 50 lb. Bags)		8-2-12-180 (Florikote Collier blend) 15 lb. per 1000 S.F. (7 - 50 lb. bags)	14-14-14-90 7 lbs. per 1000 S.F. (1 - 50 lb. bag)
Nov-14				20-20-20 2.5 lbs./25 gal. H2O per 1000 S.F. (14 lbs.)
Dec-14	Optional 21-0-0 2.2 lbs. per 1000 S.F. (2 - 50 lb. Bags)			
Optional- At maintenance Consultants direction. Blooming Plants - Bougainvillea, Indian Hawthorn, Plumbago				
Optional: Add to pest and/or disease control sprays for shrubs and turf: Ferromec AC 15-0-0 plus 6% iron, 3% sulfur @ 1.5 gal./100 gal. H2O				
Do not apply to any flower buds or blossoms in flower.				
